

CDOT NHPP 0091-044 Frisco Main St to Iron Springs

Schedule Overview


Phase 2A	Duration	Night Work/Full Closures
Remove/patch existing medians	May	
Line G drainage pipe	May-June	
Line K drainage pipe	May-June	Yes @ Main Street
Main Street Corners	May- Mid June	
8 th Street SB Right turn	May- Mid June	

Phase 2A-1	Duration	Night Work/Full Closures
Shift Traffic to SB Alignment	June	
Construct NB lanes	June-Late July	

Phase 2B	Duration	Night Work/Full Closures
Milestone	July 1 st – Open Temp Roundabout @ 8 th	
Shift Traffic to NB Alignment	Late July	Yes @ Main
Construct SB lanes	Late July-September	

Phase 2C	Duration	Night Work/Full Closures
Milestone	Sept 15 th – Completion of all HMA Paving (Besides Tapers)	
Medians, Pave tapers, Curb ramps, Cross walks	September – October	

21778 - Frisco Main to Iron Springs Phase 2A-2C

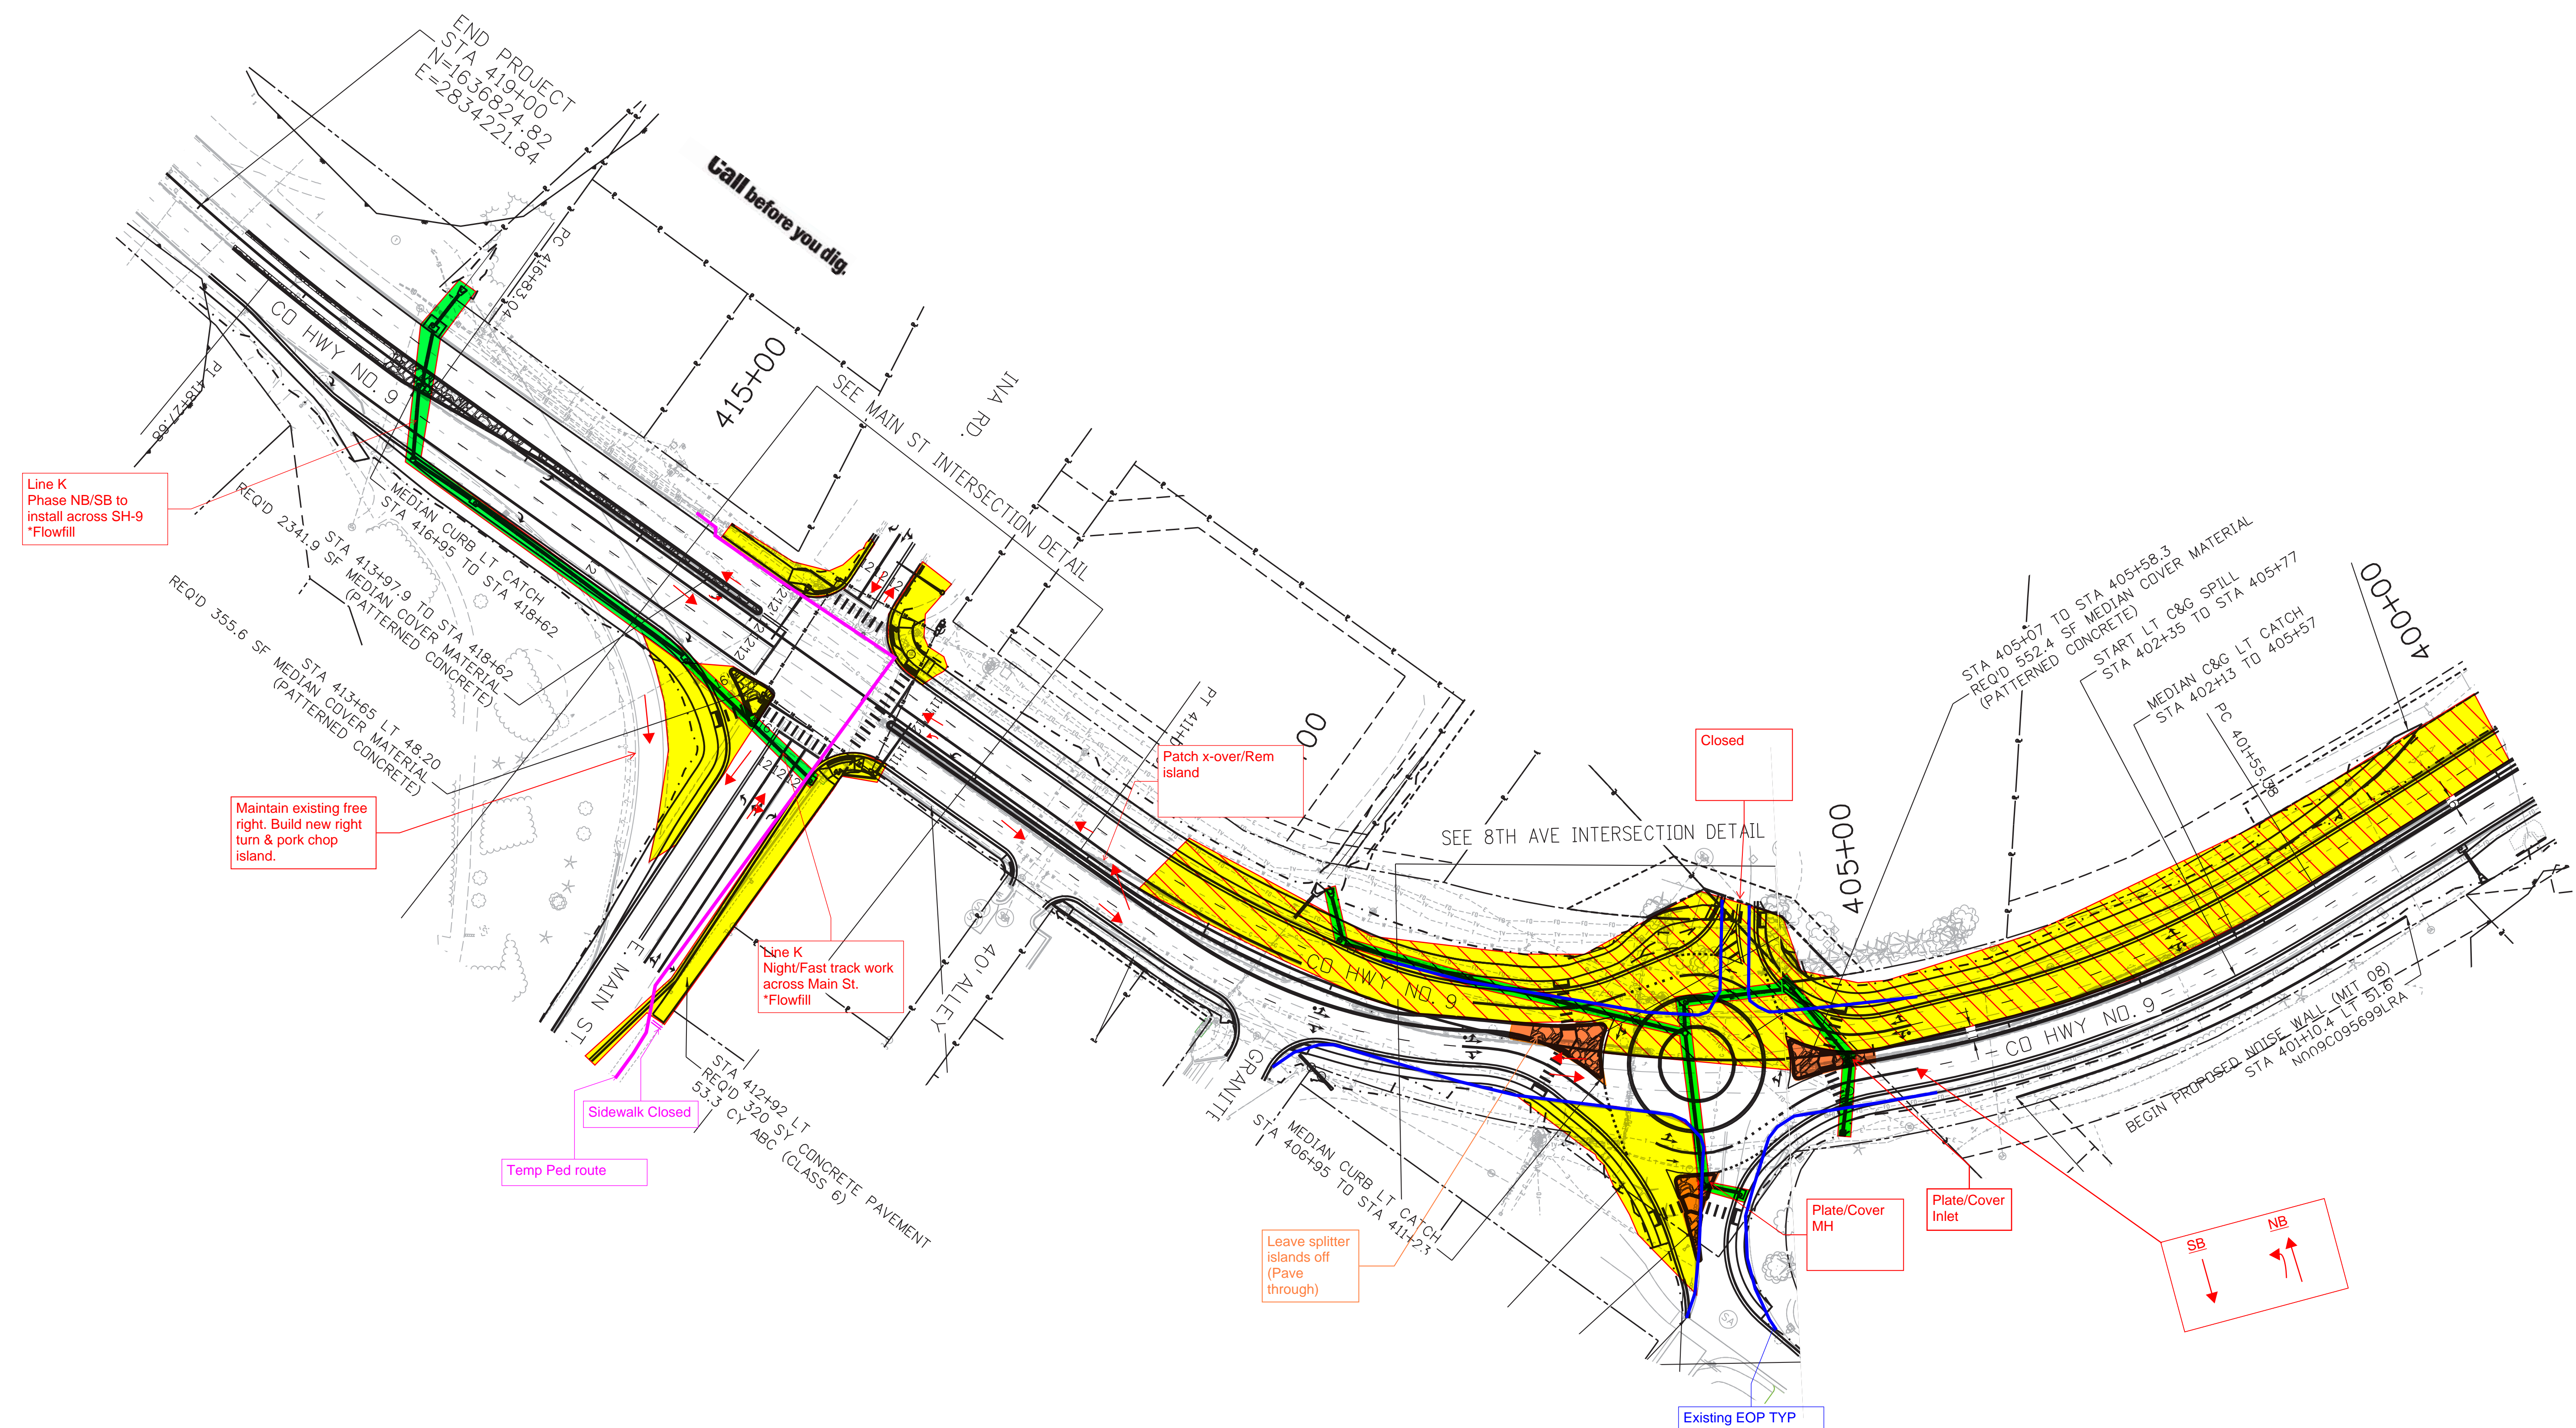


Phase 2A

- Line G
 - Line K
 - NB to STA 410+00
 - 4 Corners of Main St. (Signals, Sidewalk, Curb Ramps)
 - SB RT Turn Pocket/Curb Island
- Duration: May-June

Previously
Completed


Current
Phase

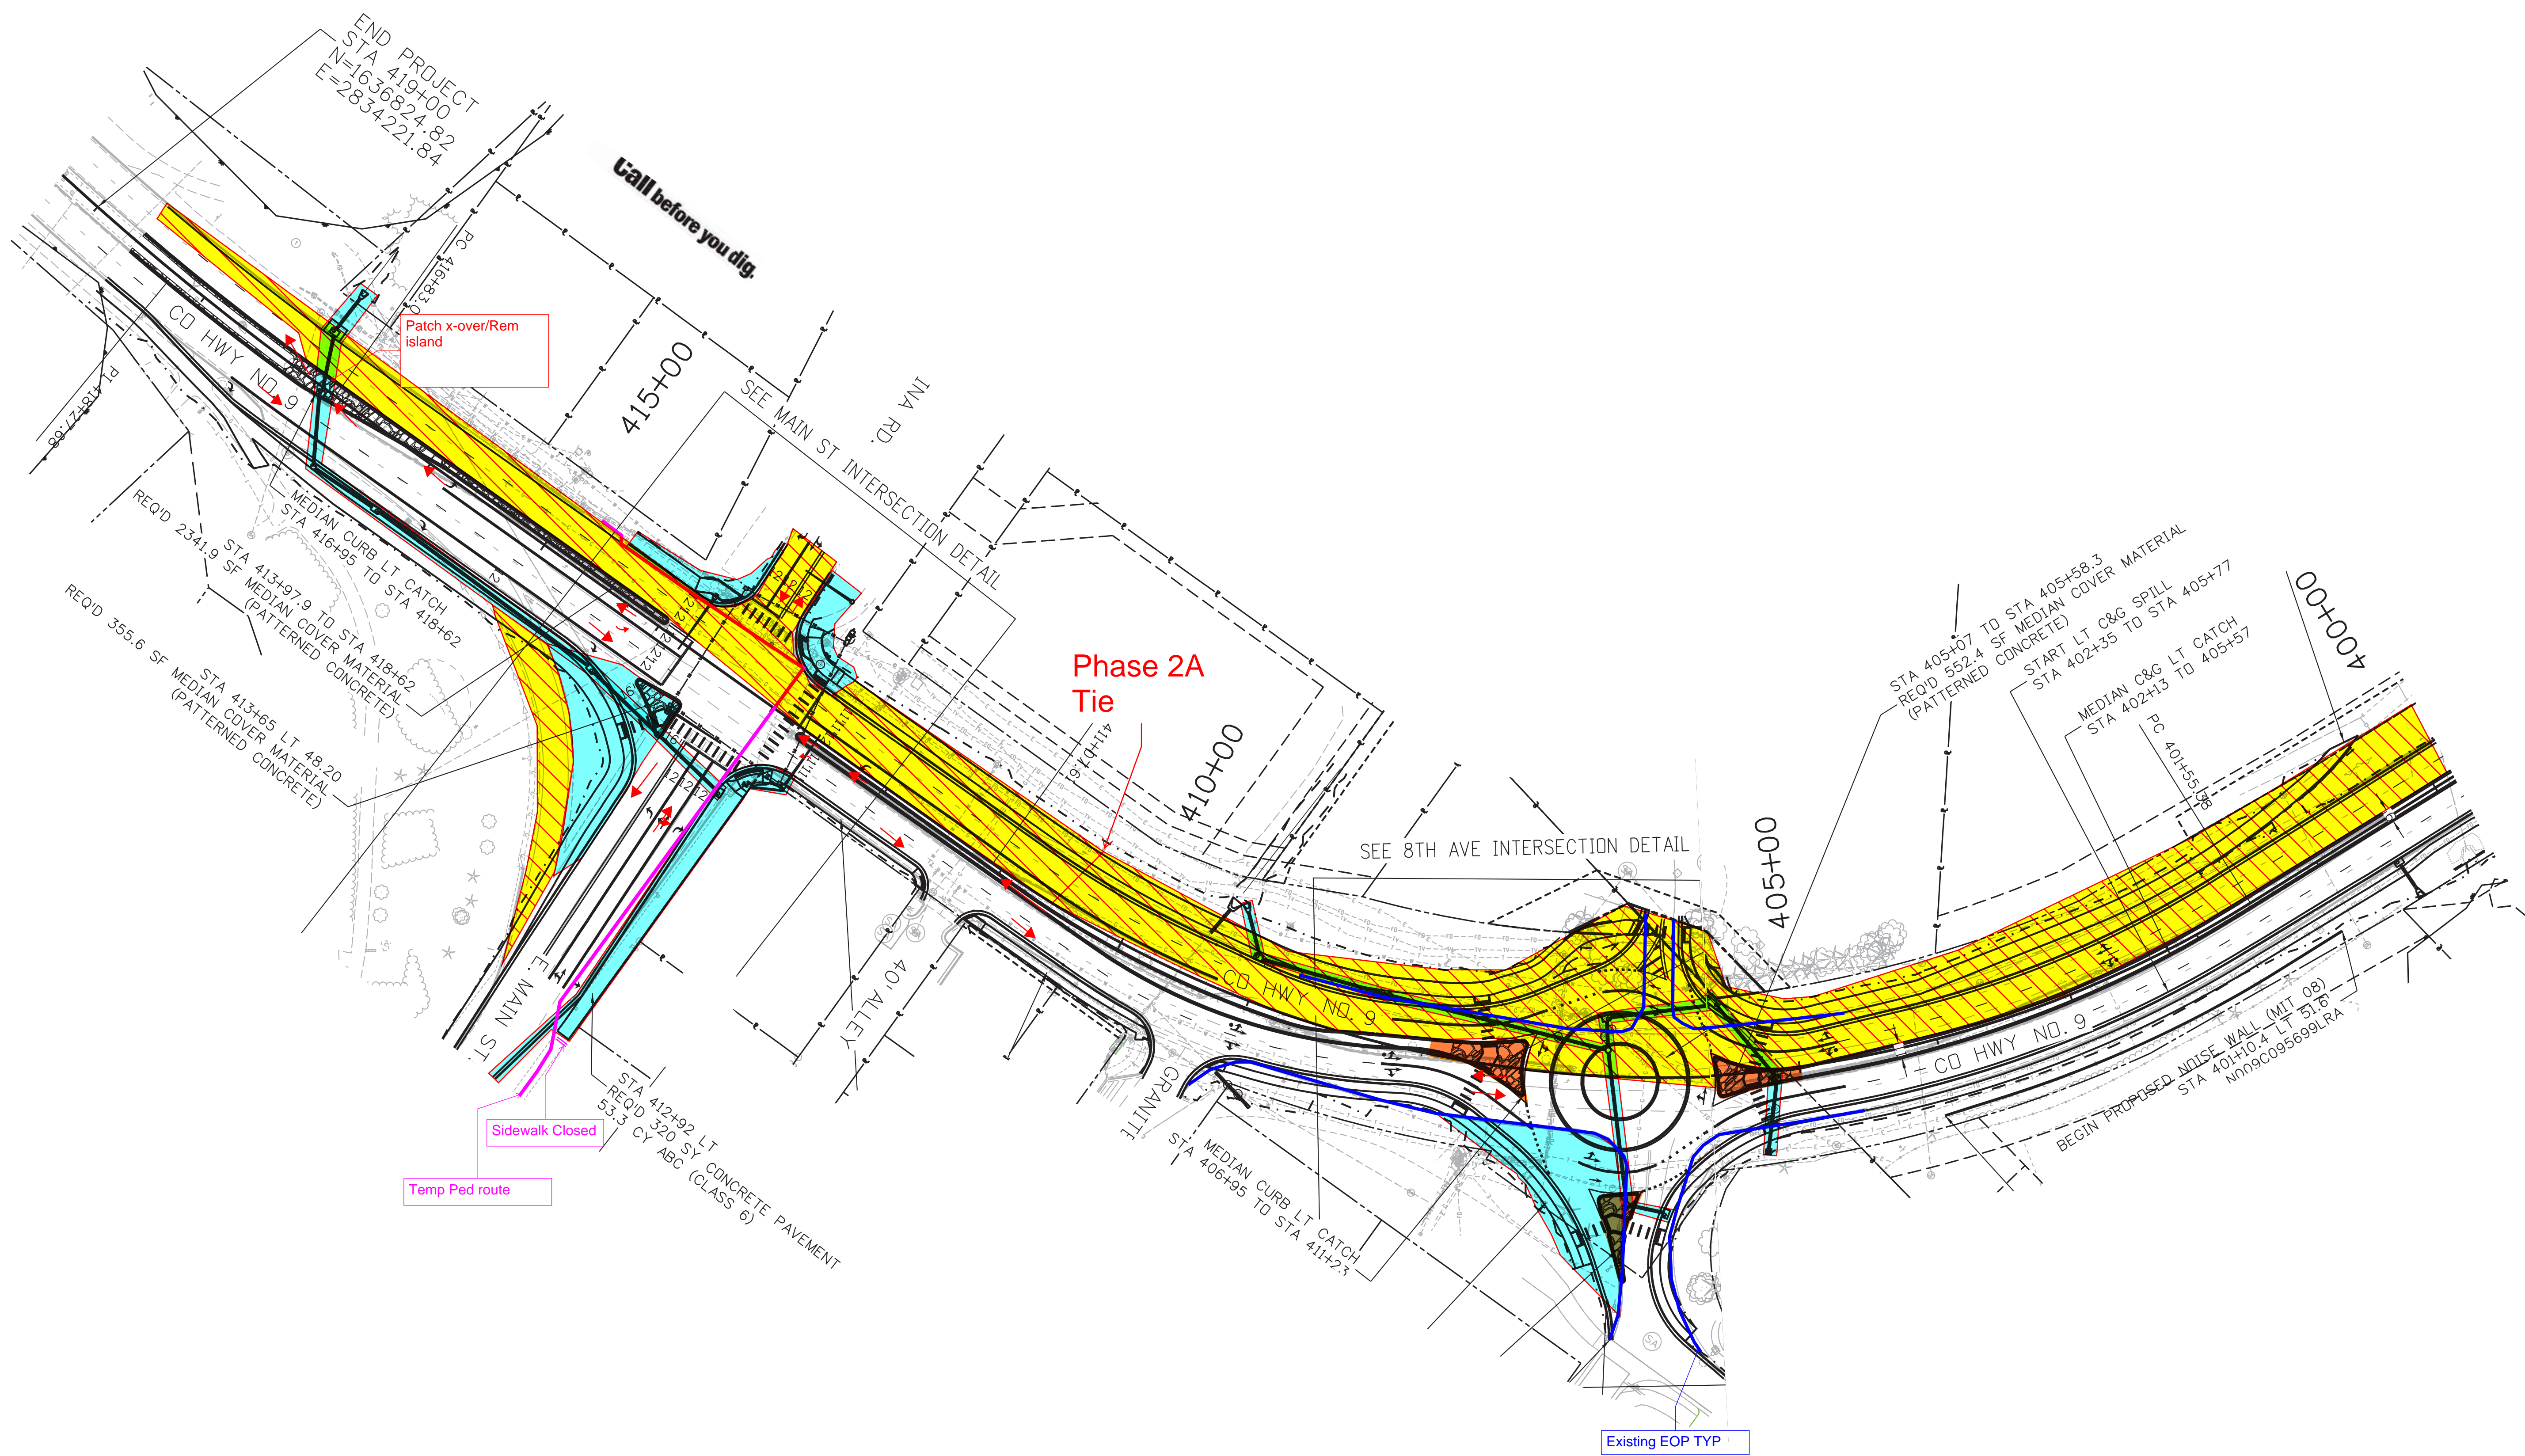

Phase 2A-1
-Shift all traffic through intersection to
SB side @ main.
-Finish NB to end of project.
Duration: June-July

Previously
Completed

Current
Phase

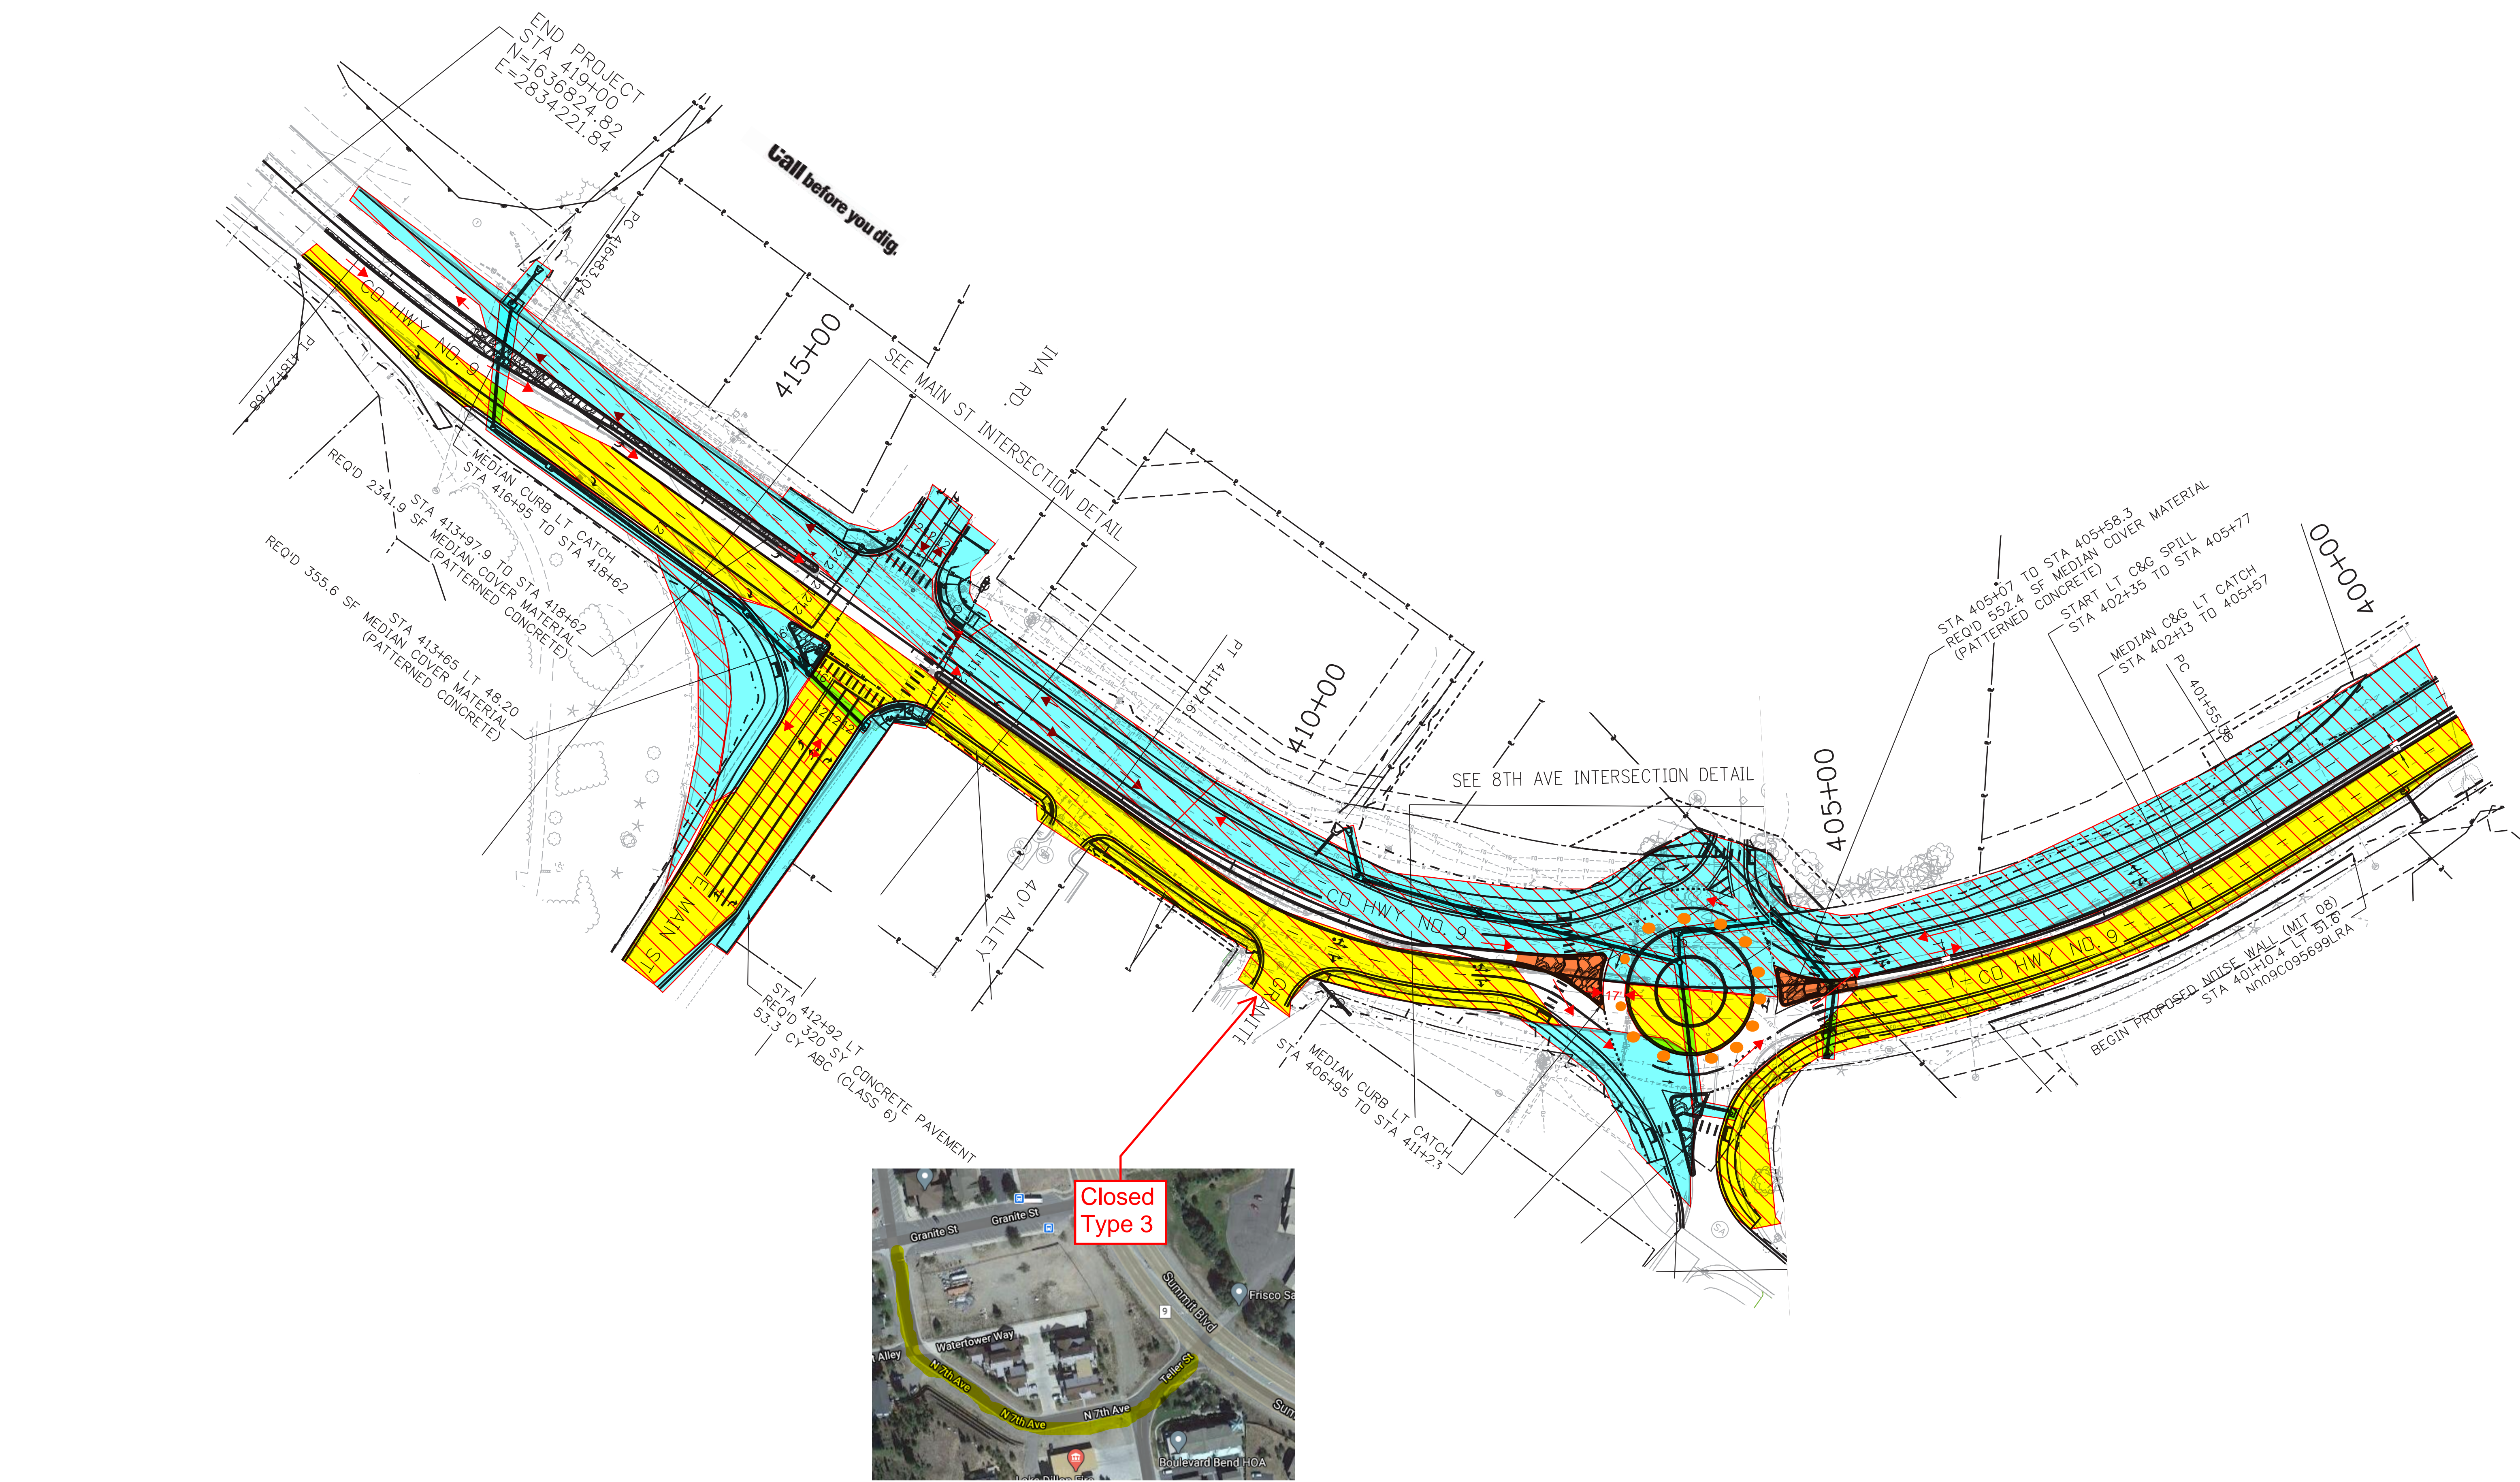


Phase 2B

- Open Temp Roundabout
- Shift Traffic to NB side of SH-9
- Mill & Pave Main Night/Fast track.

Duration: July-September

Previously
Completed

Current
Phase

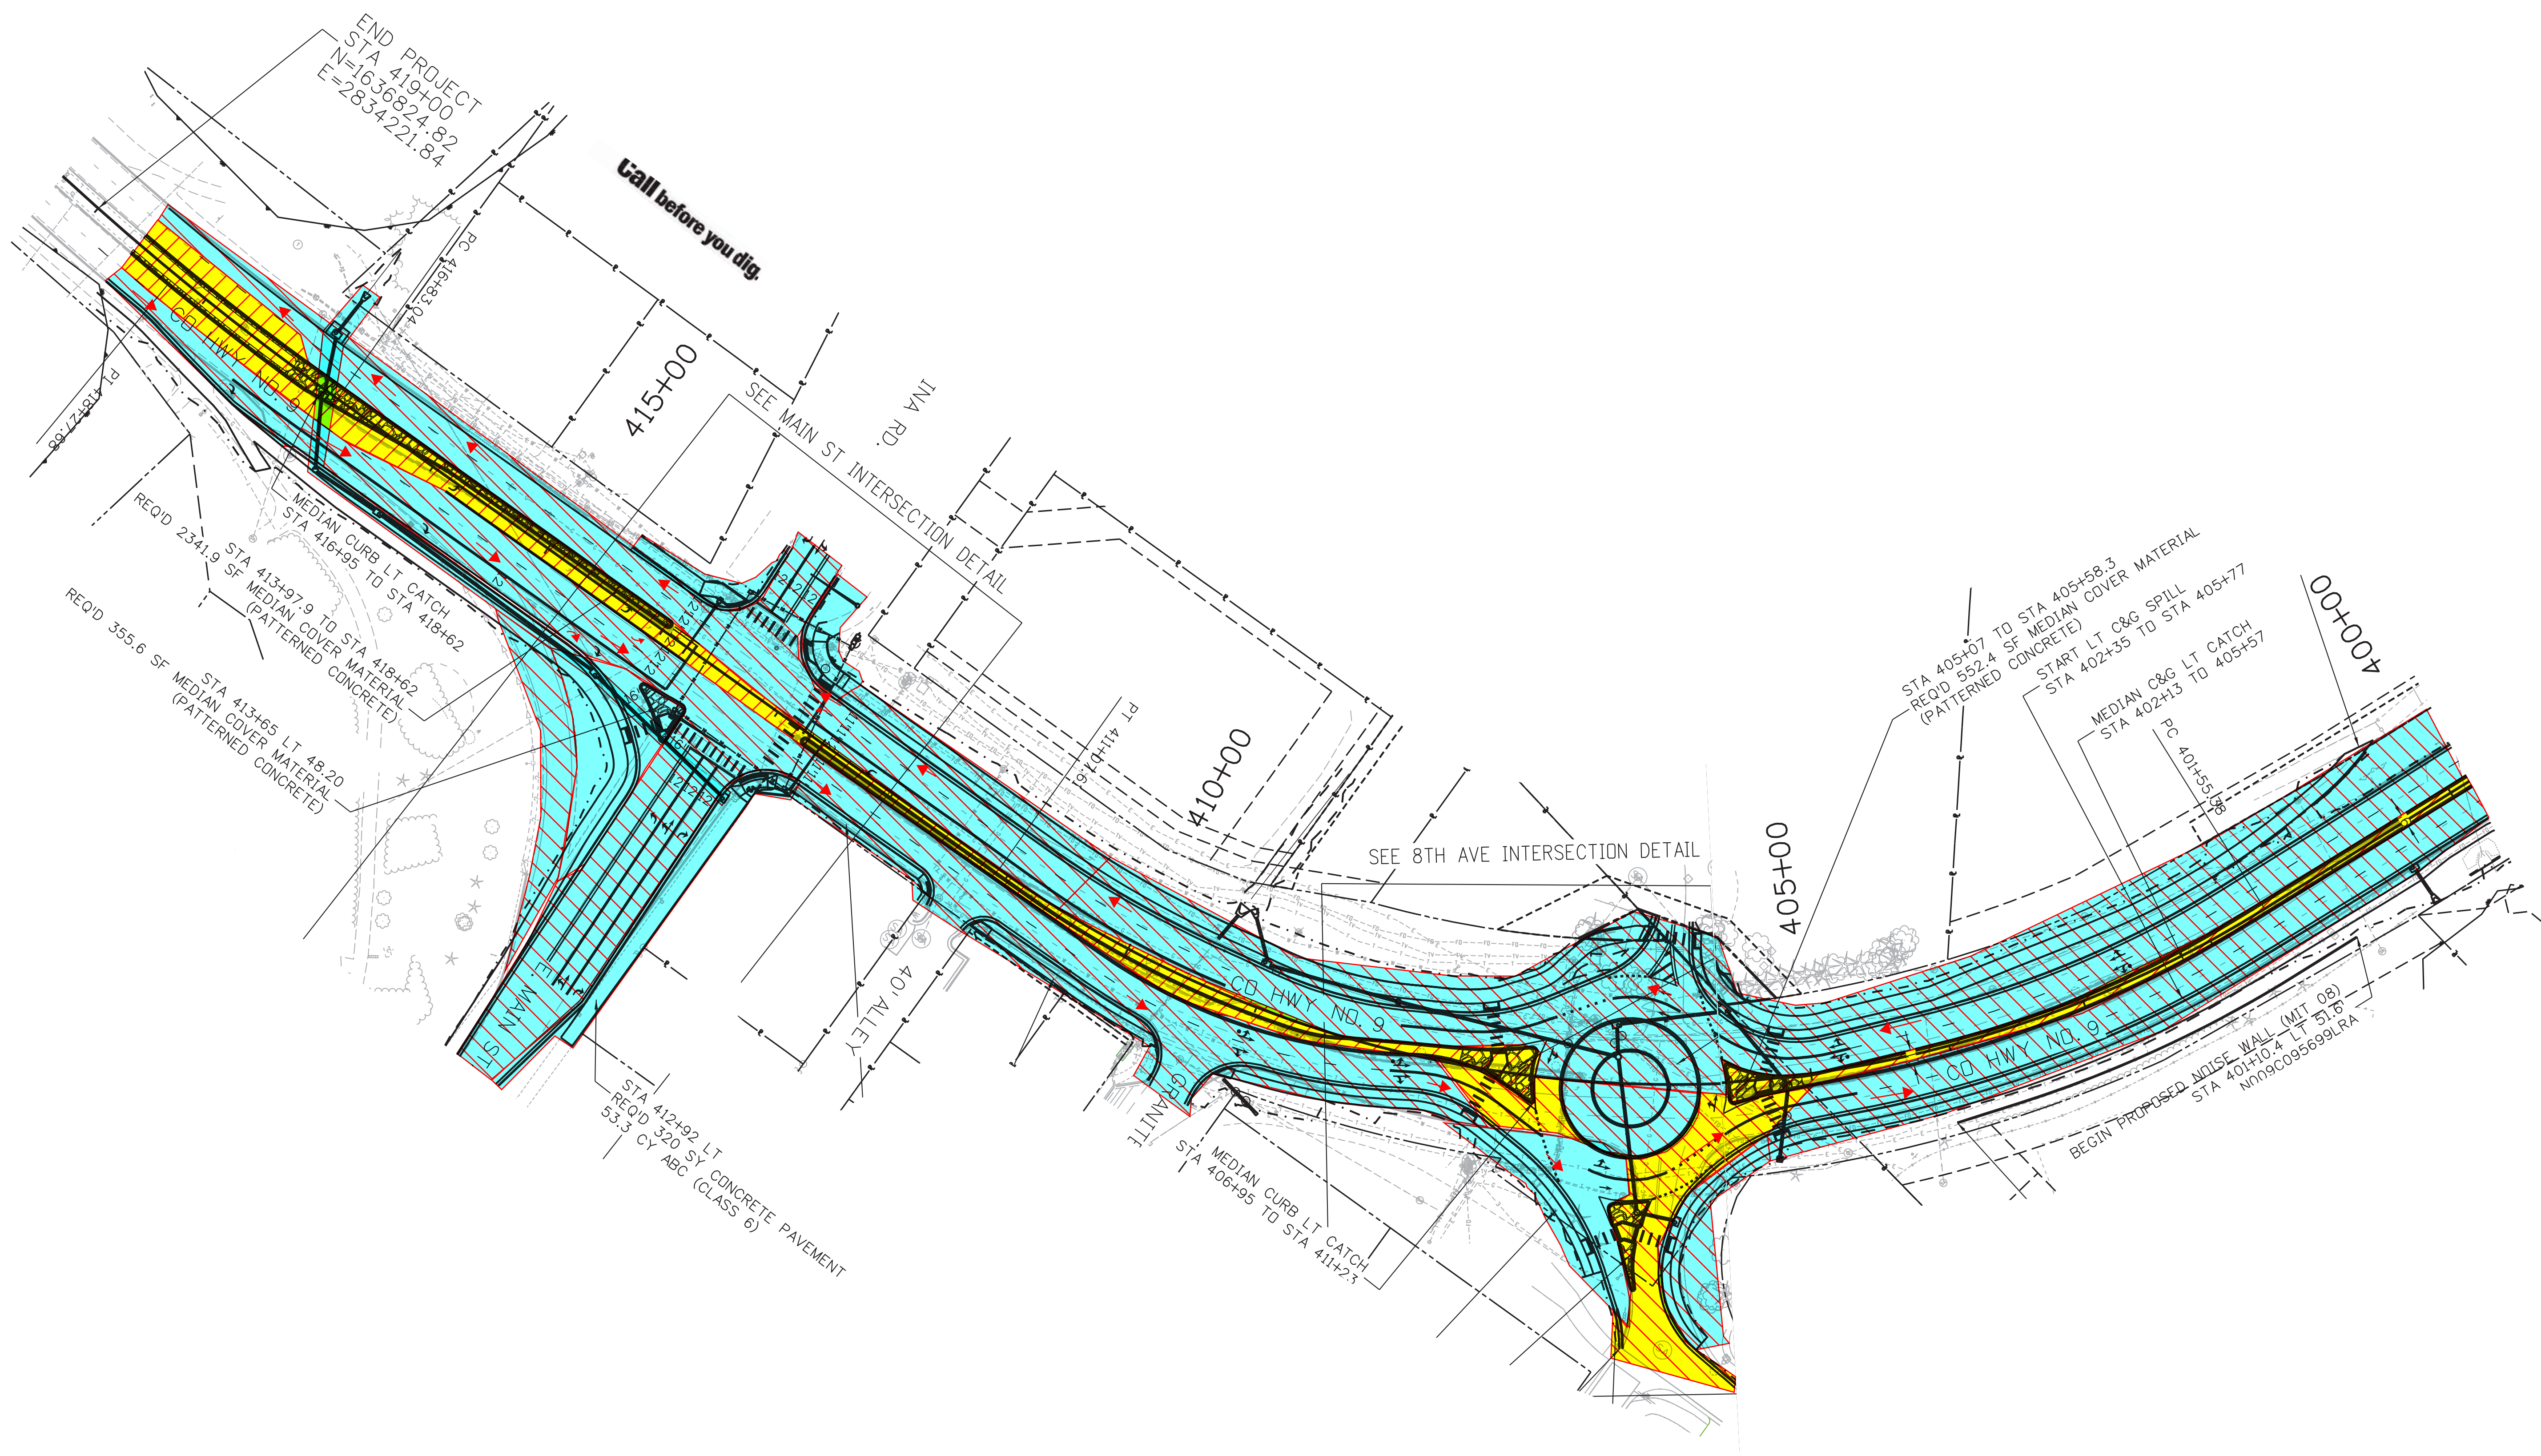

Phase 2C
-Complete Medians & Pave tapers
-Splitter islands & 8th Ave curb ramps
+ Cross walks.
Duration: September - October
